



Phase 1: May 2017 - August 2017

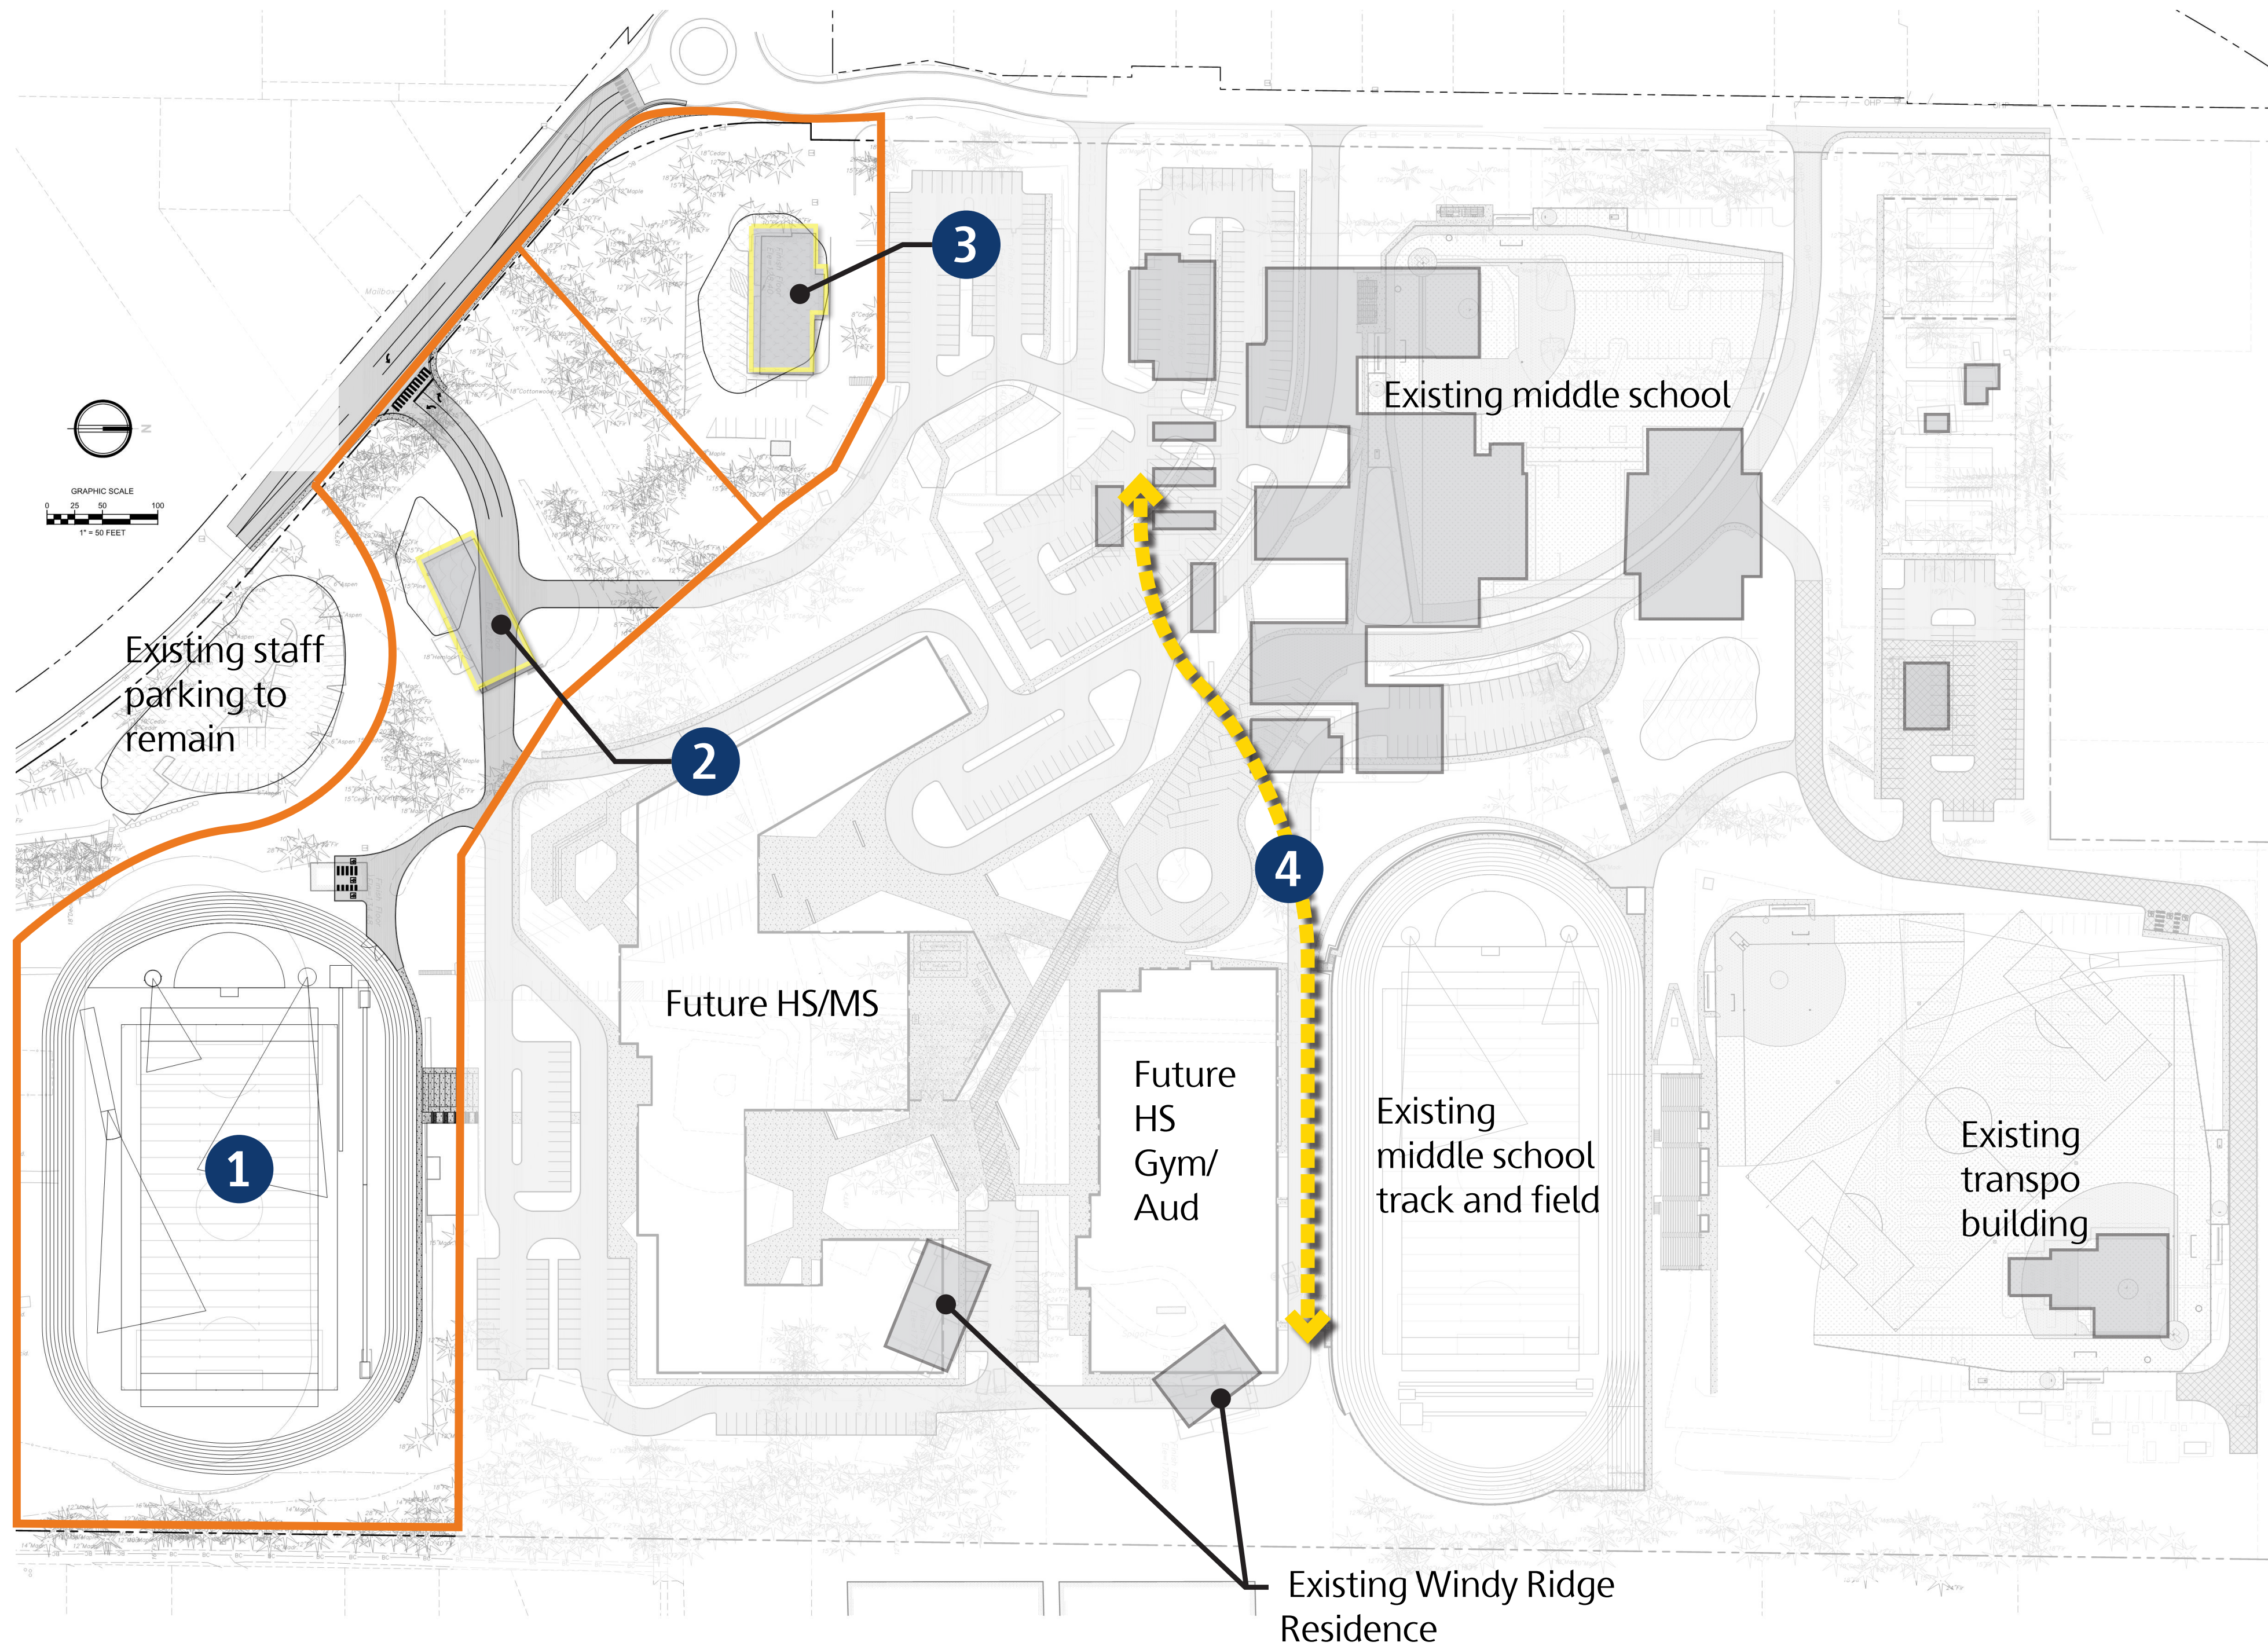

Phase 1: Early Sitework Package - Huey Field

- 1 Upgrade existing high school field after varsity athletics are complete.
- 2 Demo Science Kit Building (April 2017).
- 3 Demo Alternative High School building (July 2017).
- 4 Construct new access road to North Windy Ridge property (July 2017).


Phase 2: June 2017 - September 2017

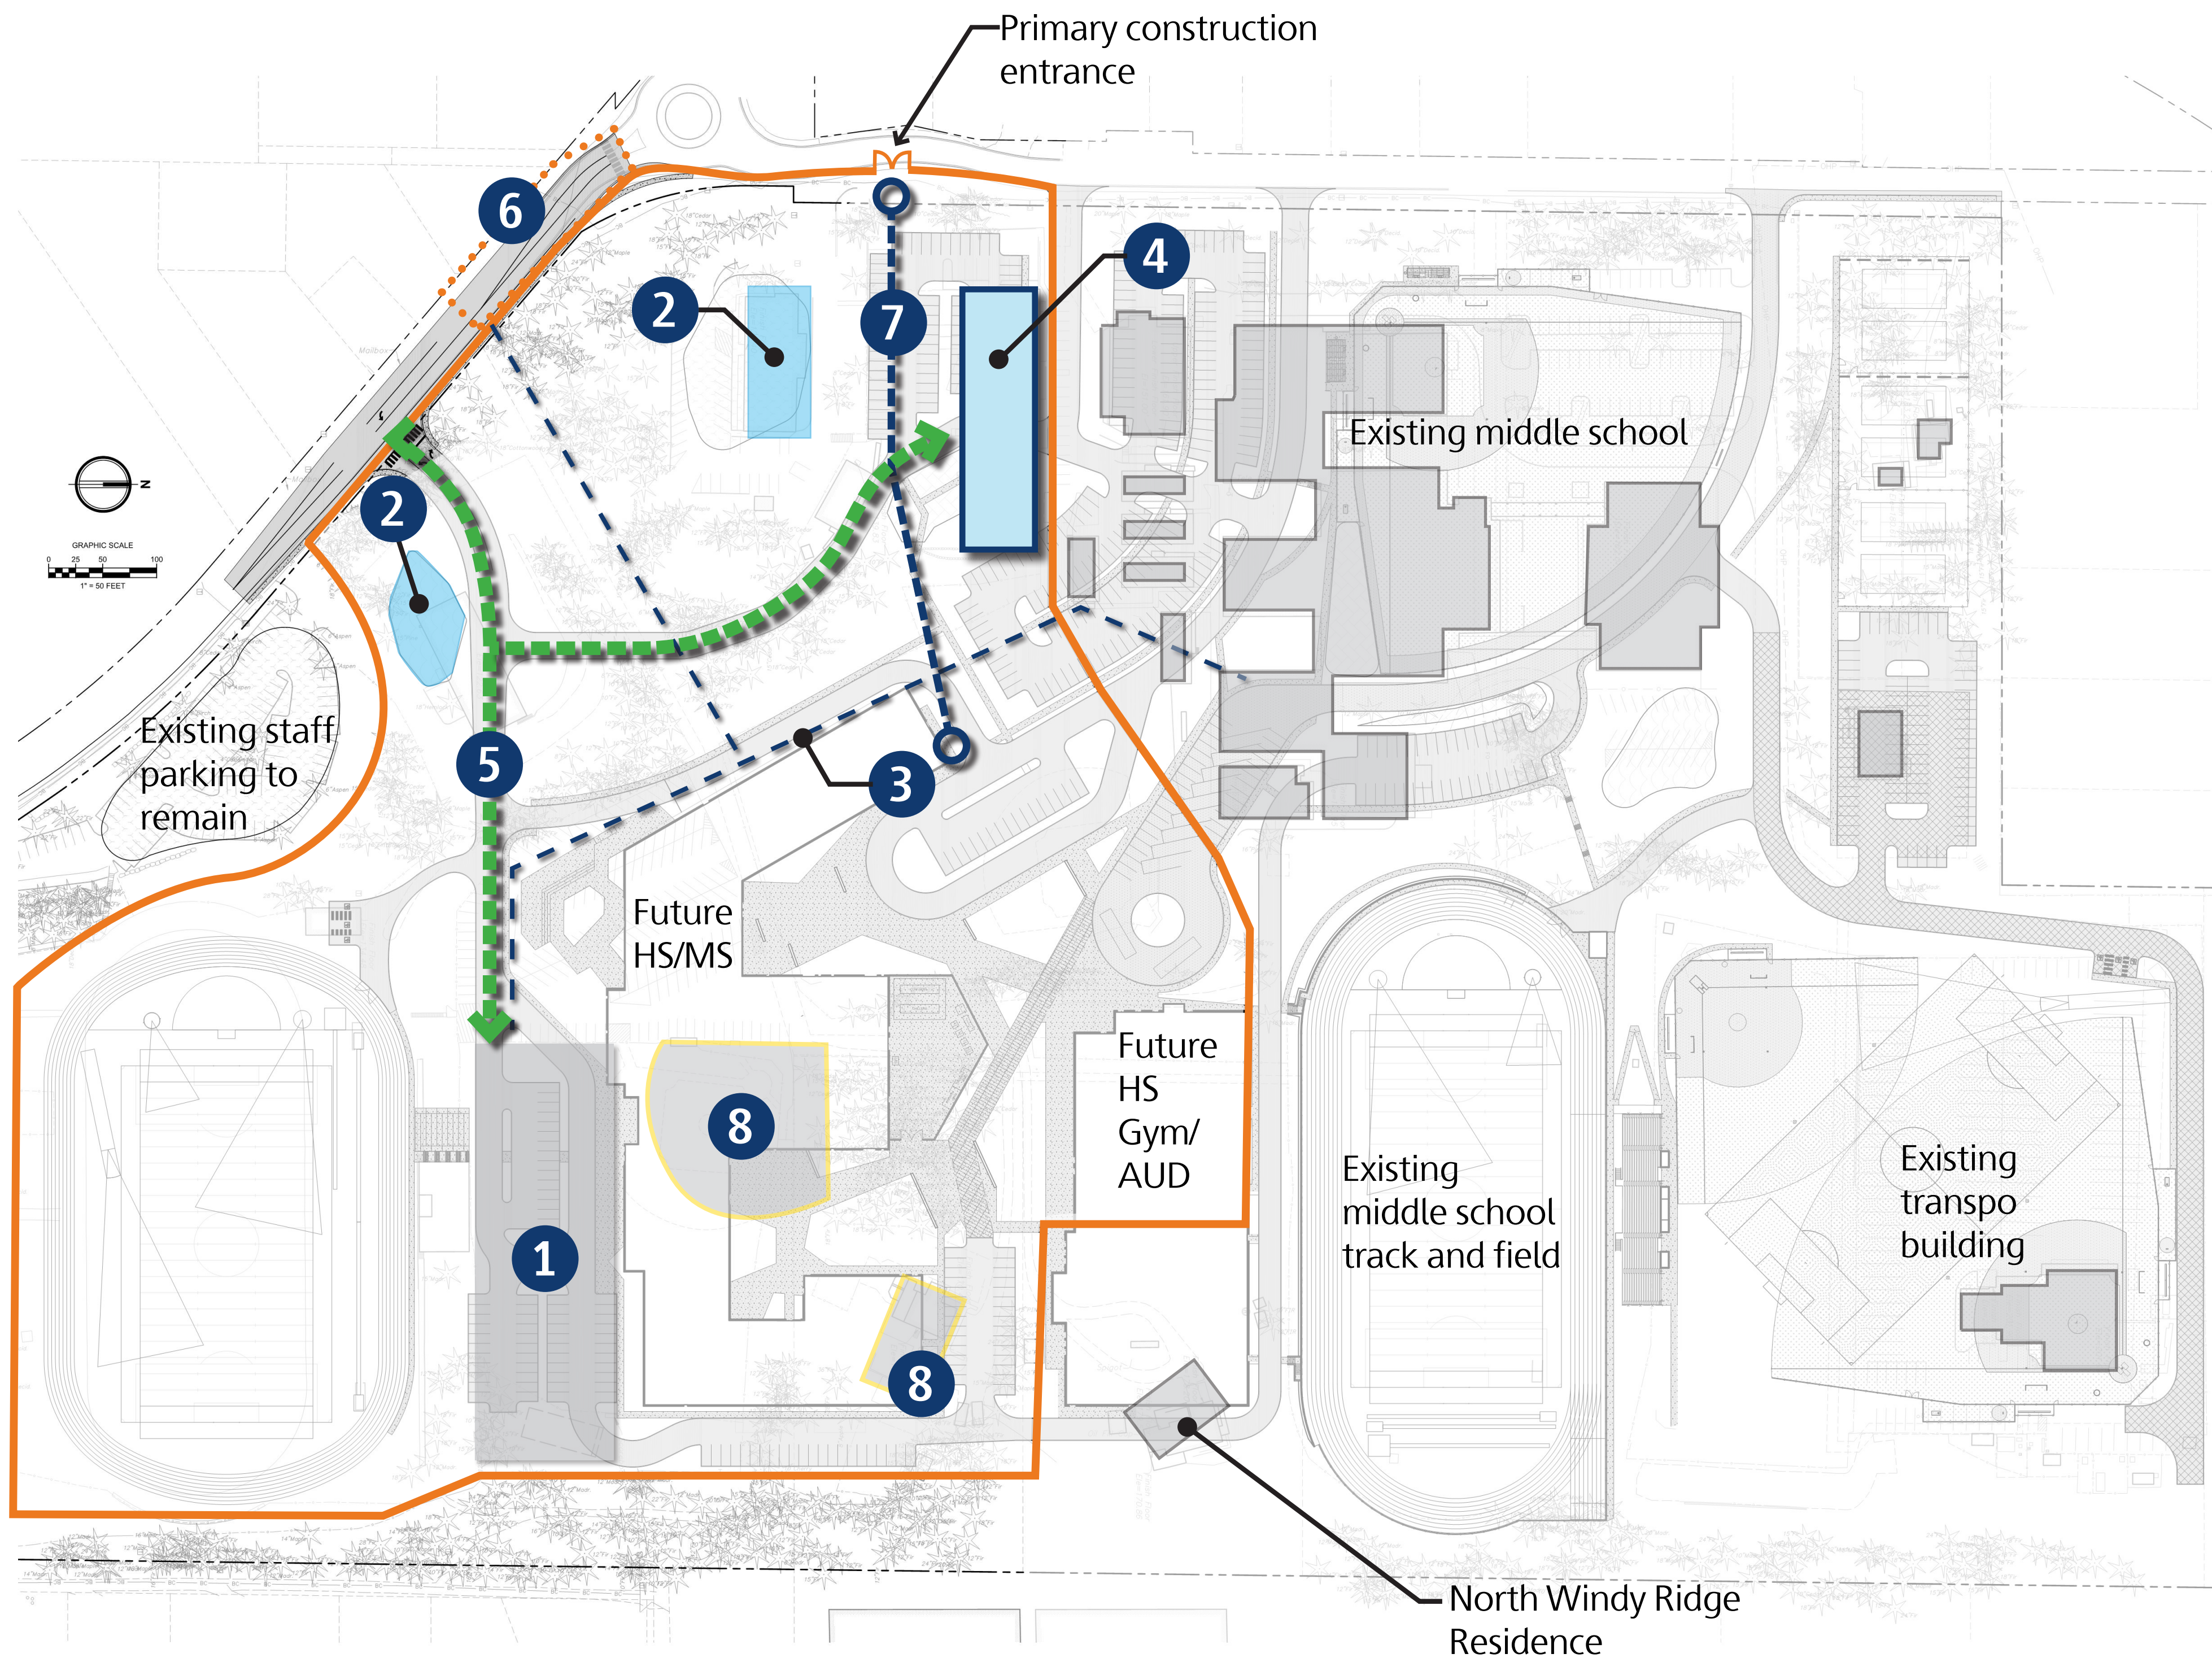

Phase 2

- 1 Construct access road and build temporary student parking north of existing high school track.
- 2 Build two storm water ponds and outlets for temporary sediment and erosion control.
- 3 Reroute utilities: power and fiber; install sanitary sewer to bypass middle school sewer line at the storm pond.
- 4 Establish contractor temporary offices at former food warehouse.
- 5 Construct new primary school access road/ temporary student parking access.
- 6 Construct frontage improvements to widen Anderson Hill Road and build new curb gutter and sidewalk.
- 7 Install sanitary sewer, gas, water main and power from Frontier to building pad.
- 8 Demo South Windy Ridge Residence and adjacent baseball field.


Phase 3a: September 2017 - November 2017

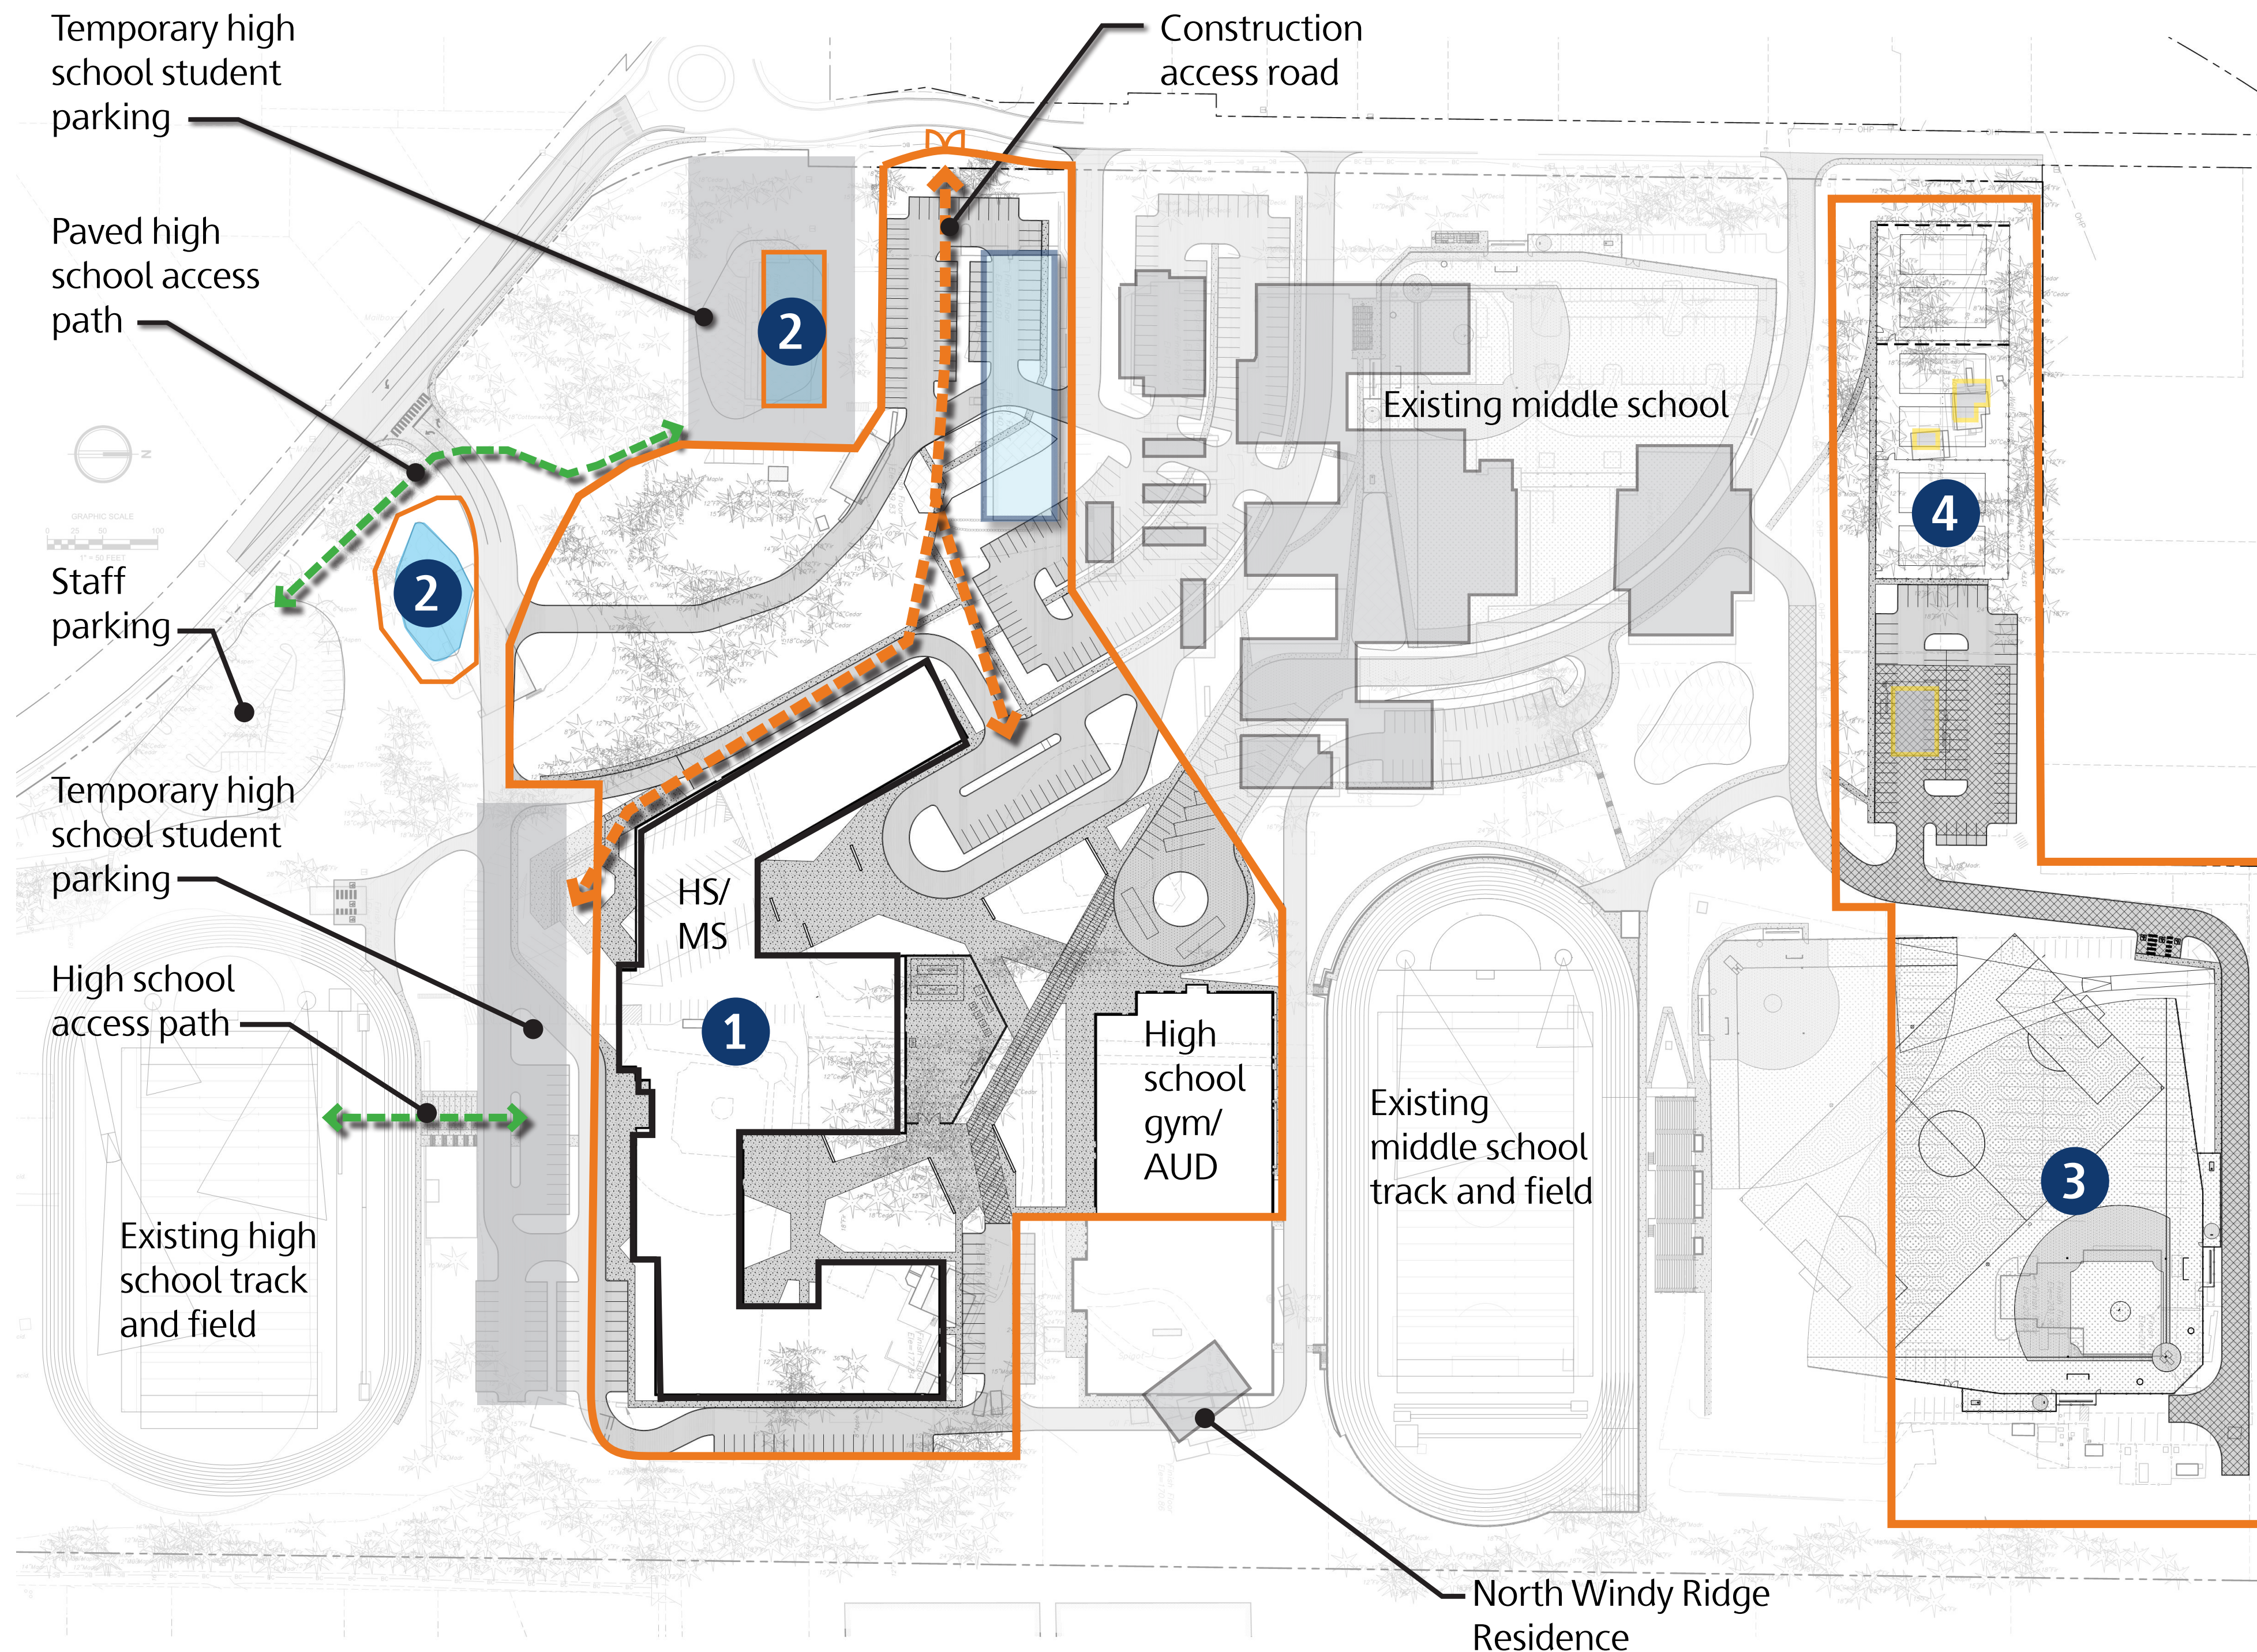

Phase 3a:

- 1 Grading within building work limits and establish building pad subgrade; begin classroom building construction.
- 2 Install/maintain erosion and sediment control measures.
- 3 Existing asphalt for construction laydown and craft parking.
- 4 Demo trees/buildings to provide middle school evacuation area during next phase when middle school track is offline.


Phase 3b: November 2017 - July 2019

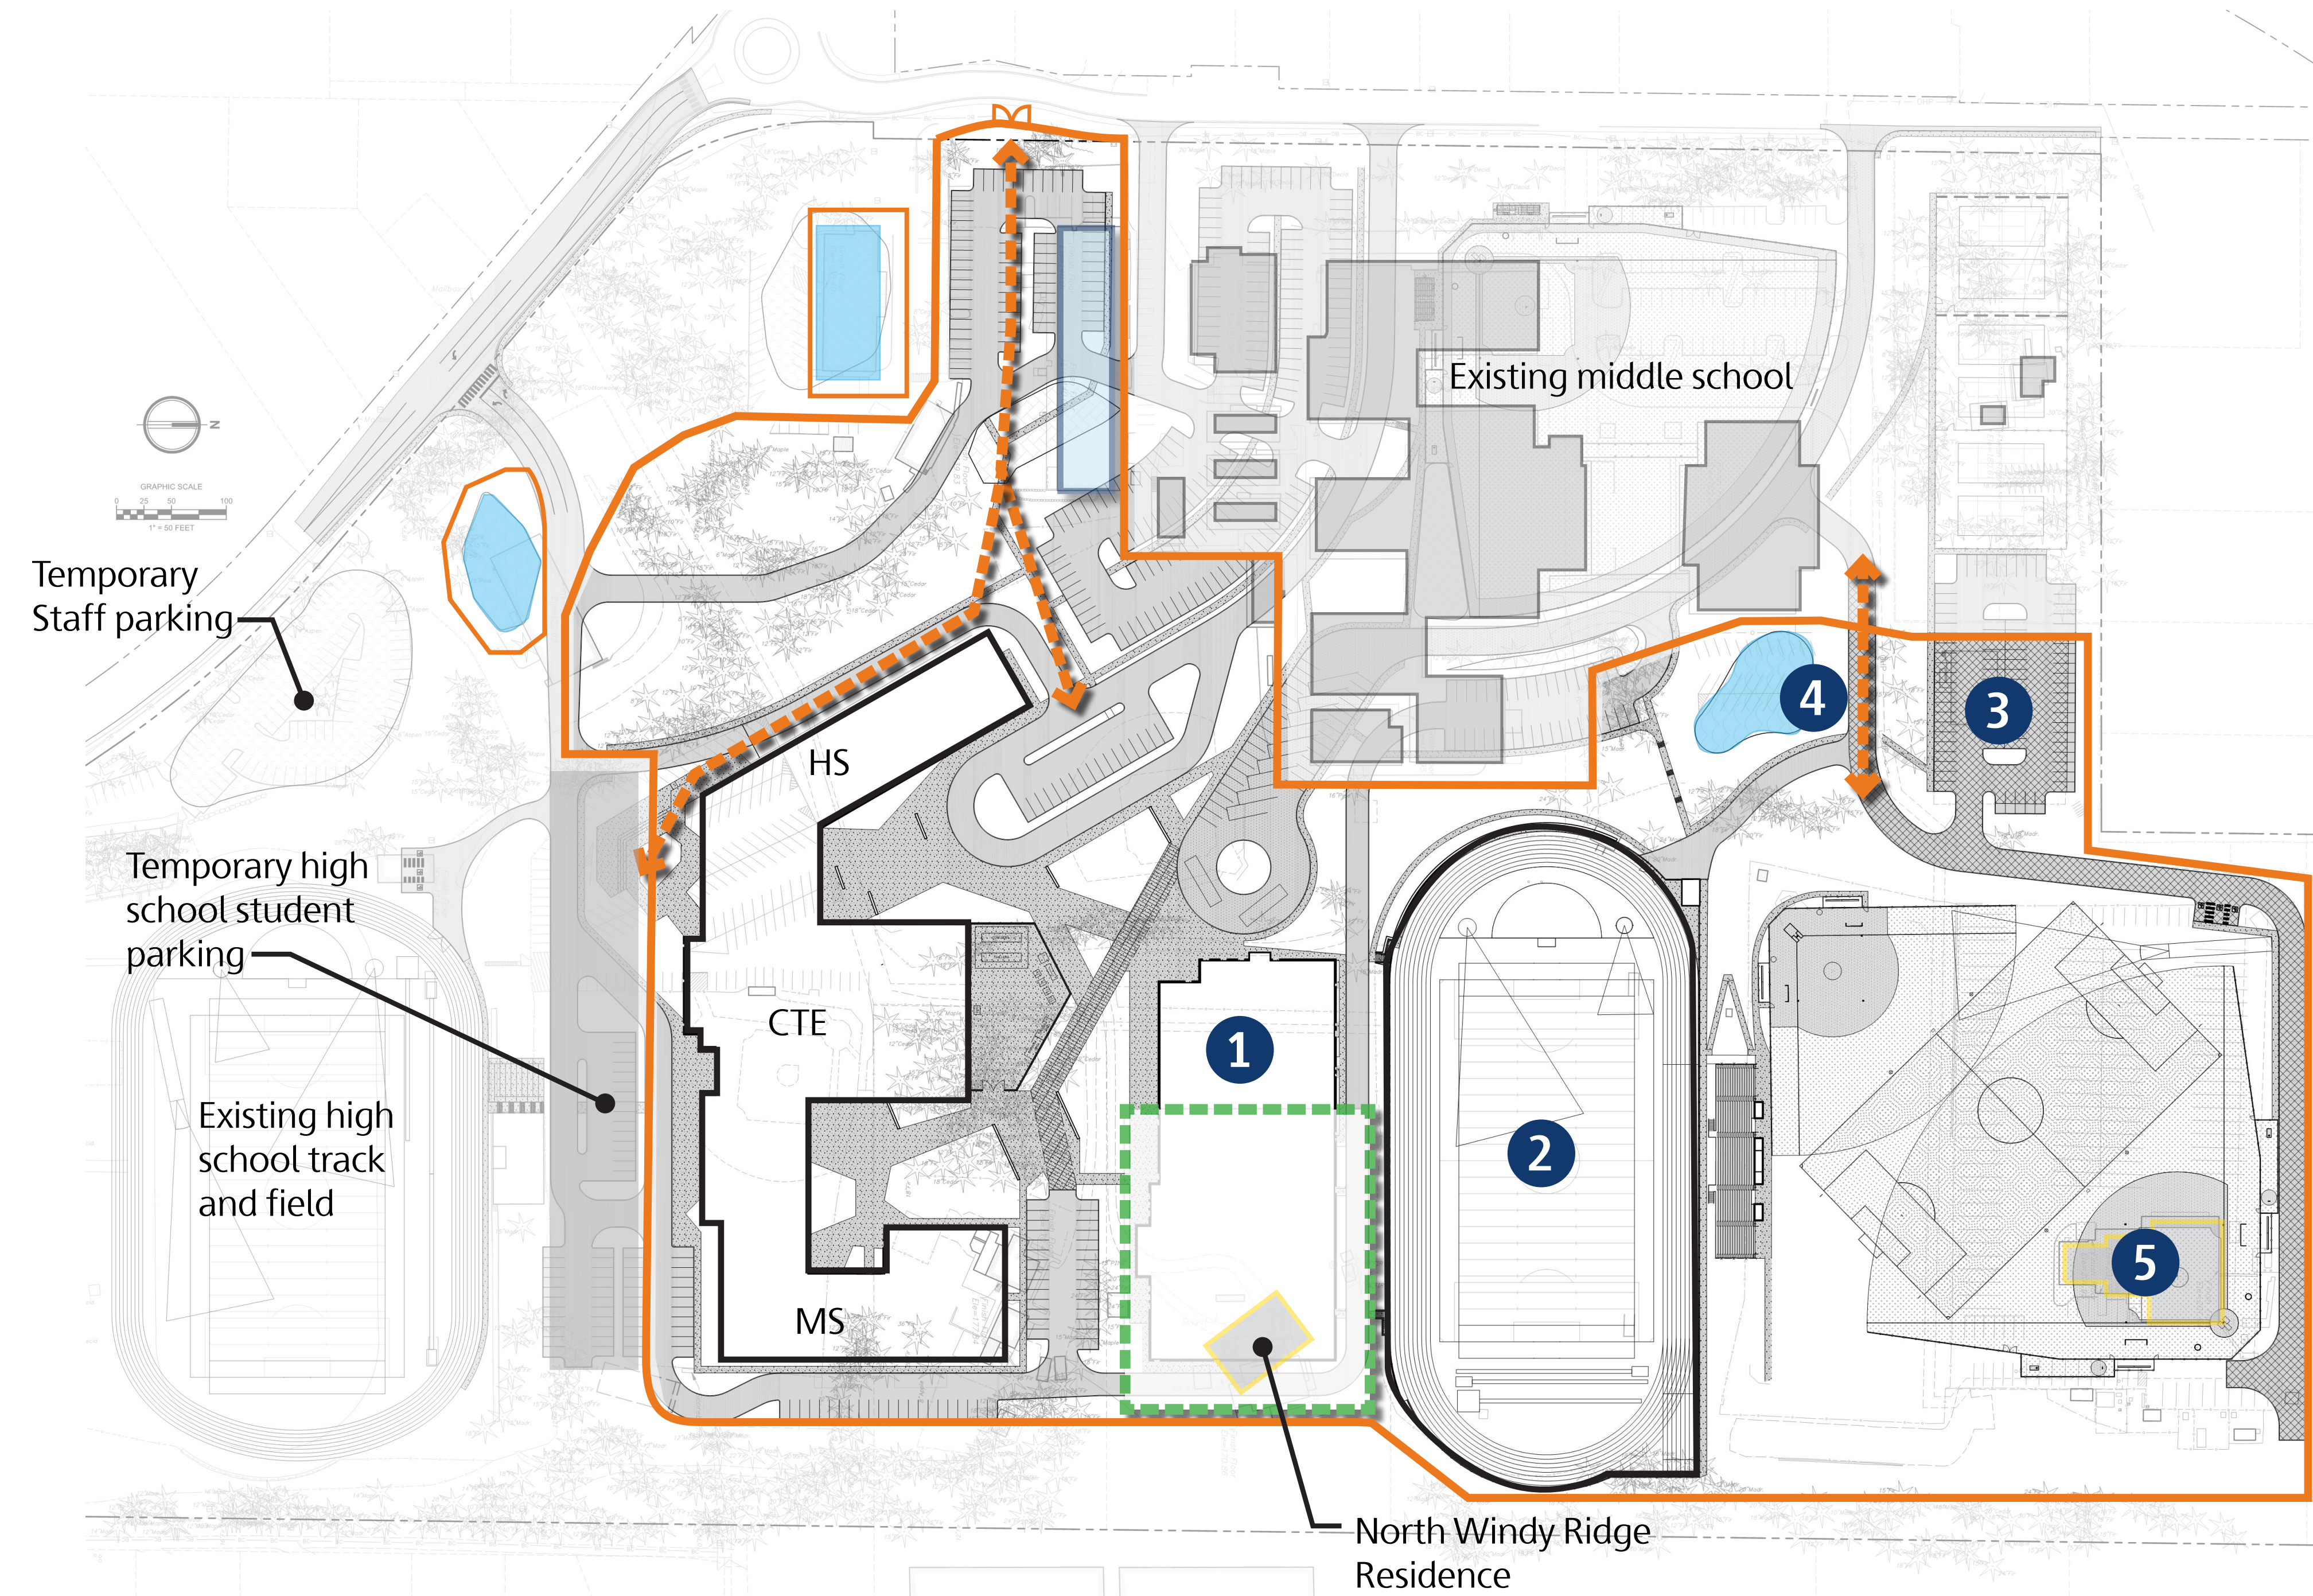

Phase 3b:

- 1 Construct Auditorium/Gym building (March 2018 - September 2019 based on vacation of the North Windy Ridge Residence).
- 2 Construct synthetic turf field and track at existing middle school (May 2018 - August 2018).
- 3 Auxiliary construction parking.
- 4 Construct new pond adjacent to existing middle school gym.
- 5 Demo existing asphalt at former transportation facility, alternative high schools, etc.


Phase 4: July 2019 - September 2019

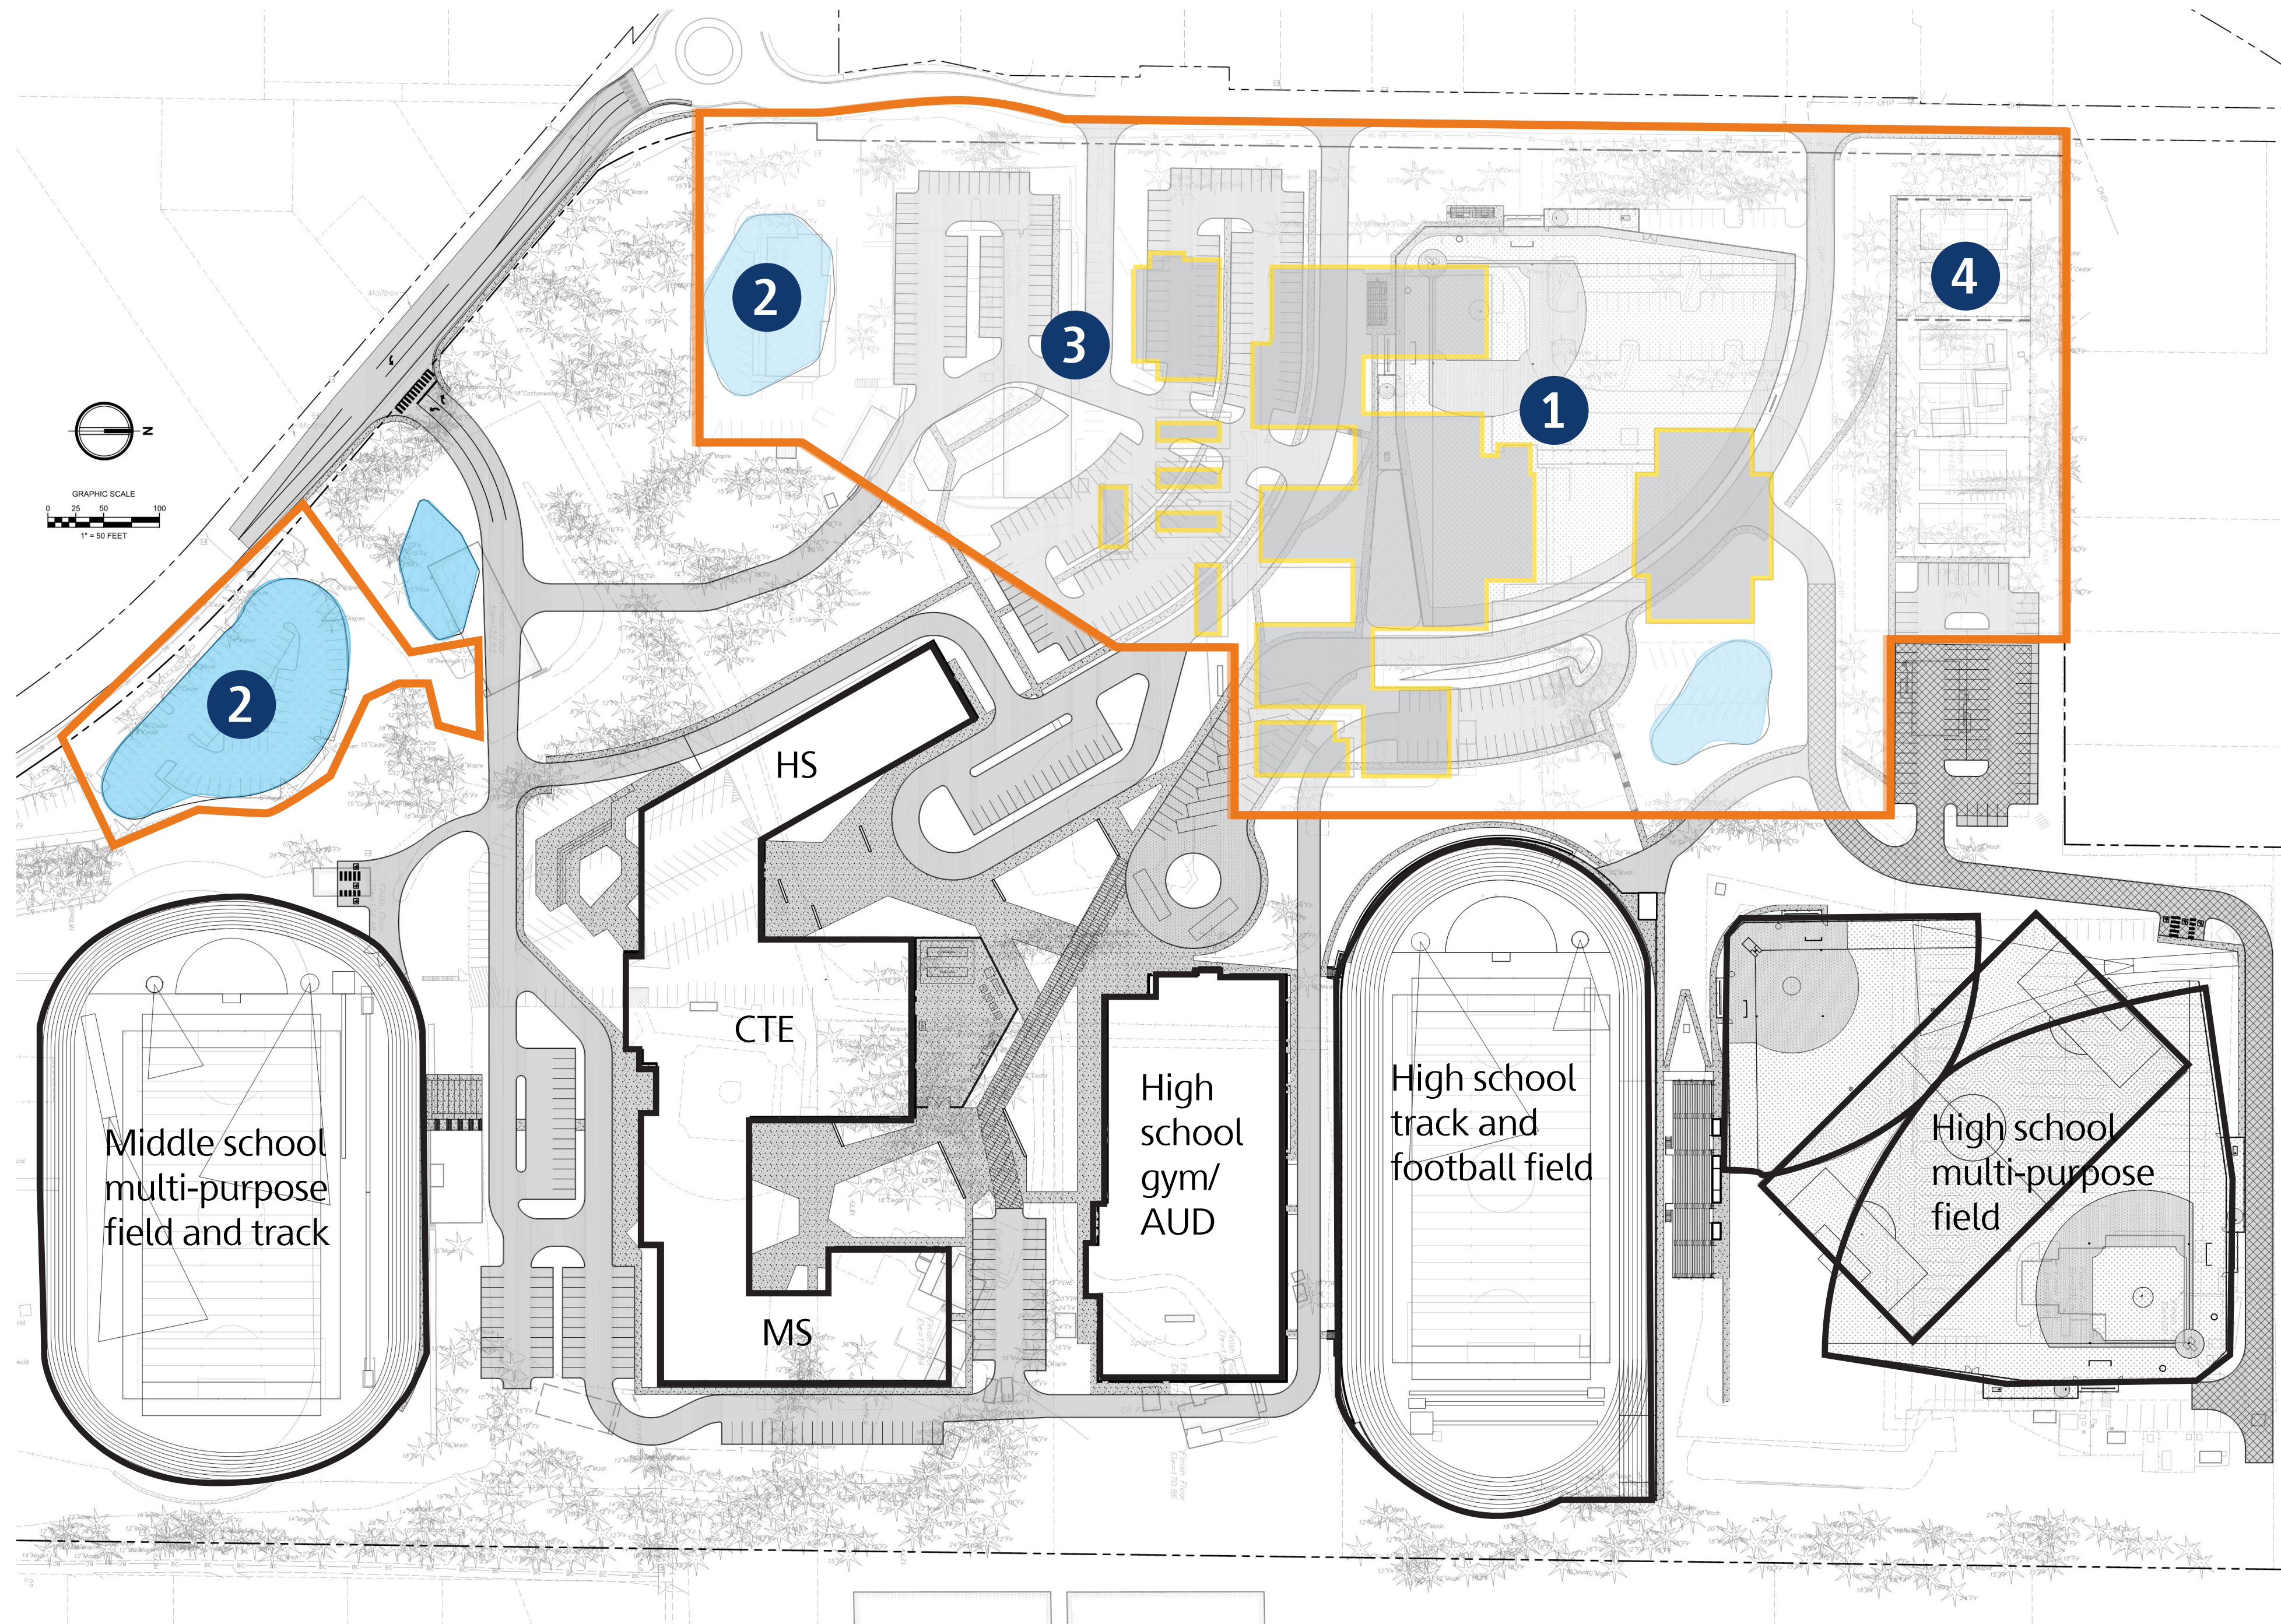

Phase 4:

- 1 Demo existing remaining middle school buildings and complete utilities: landscape, storm, sanitary.
- 2 Complete storm ponds.
- 3 Pave parking and bus access.
- 4 Construct tennis courts.

Phase 5: September 2019 - November 2019

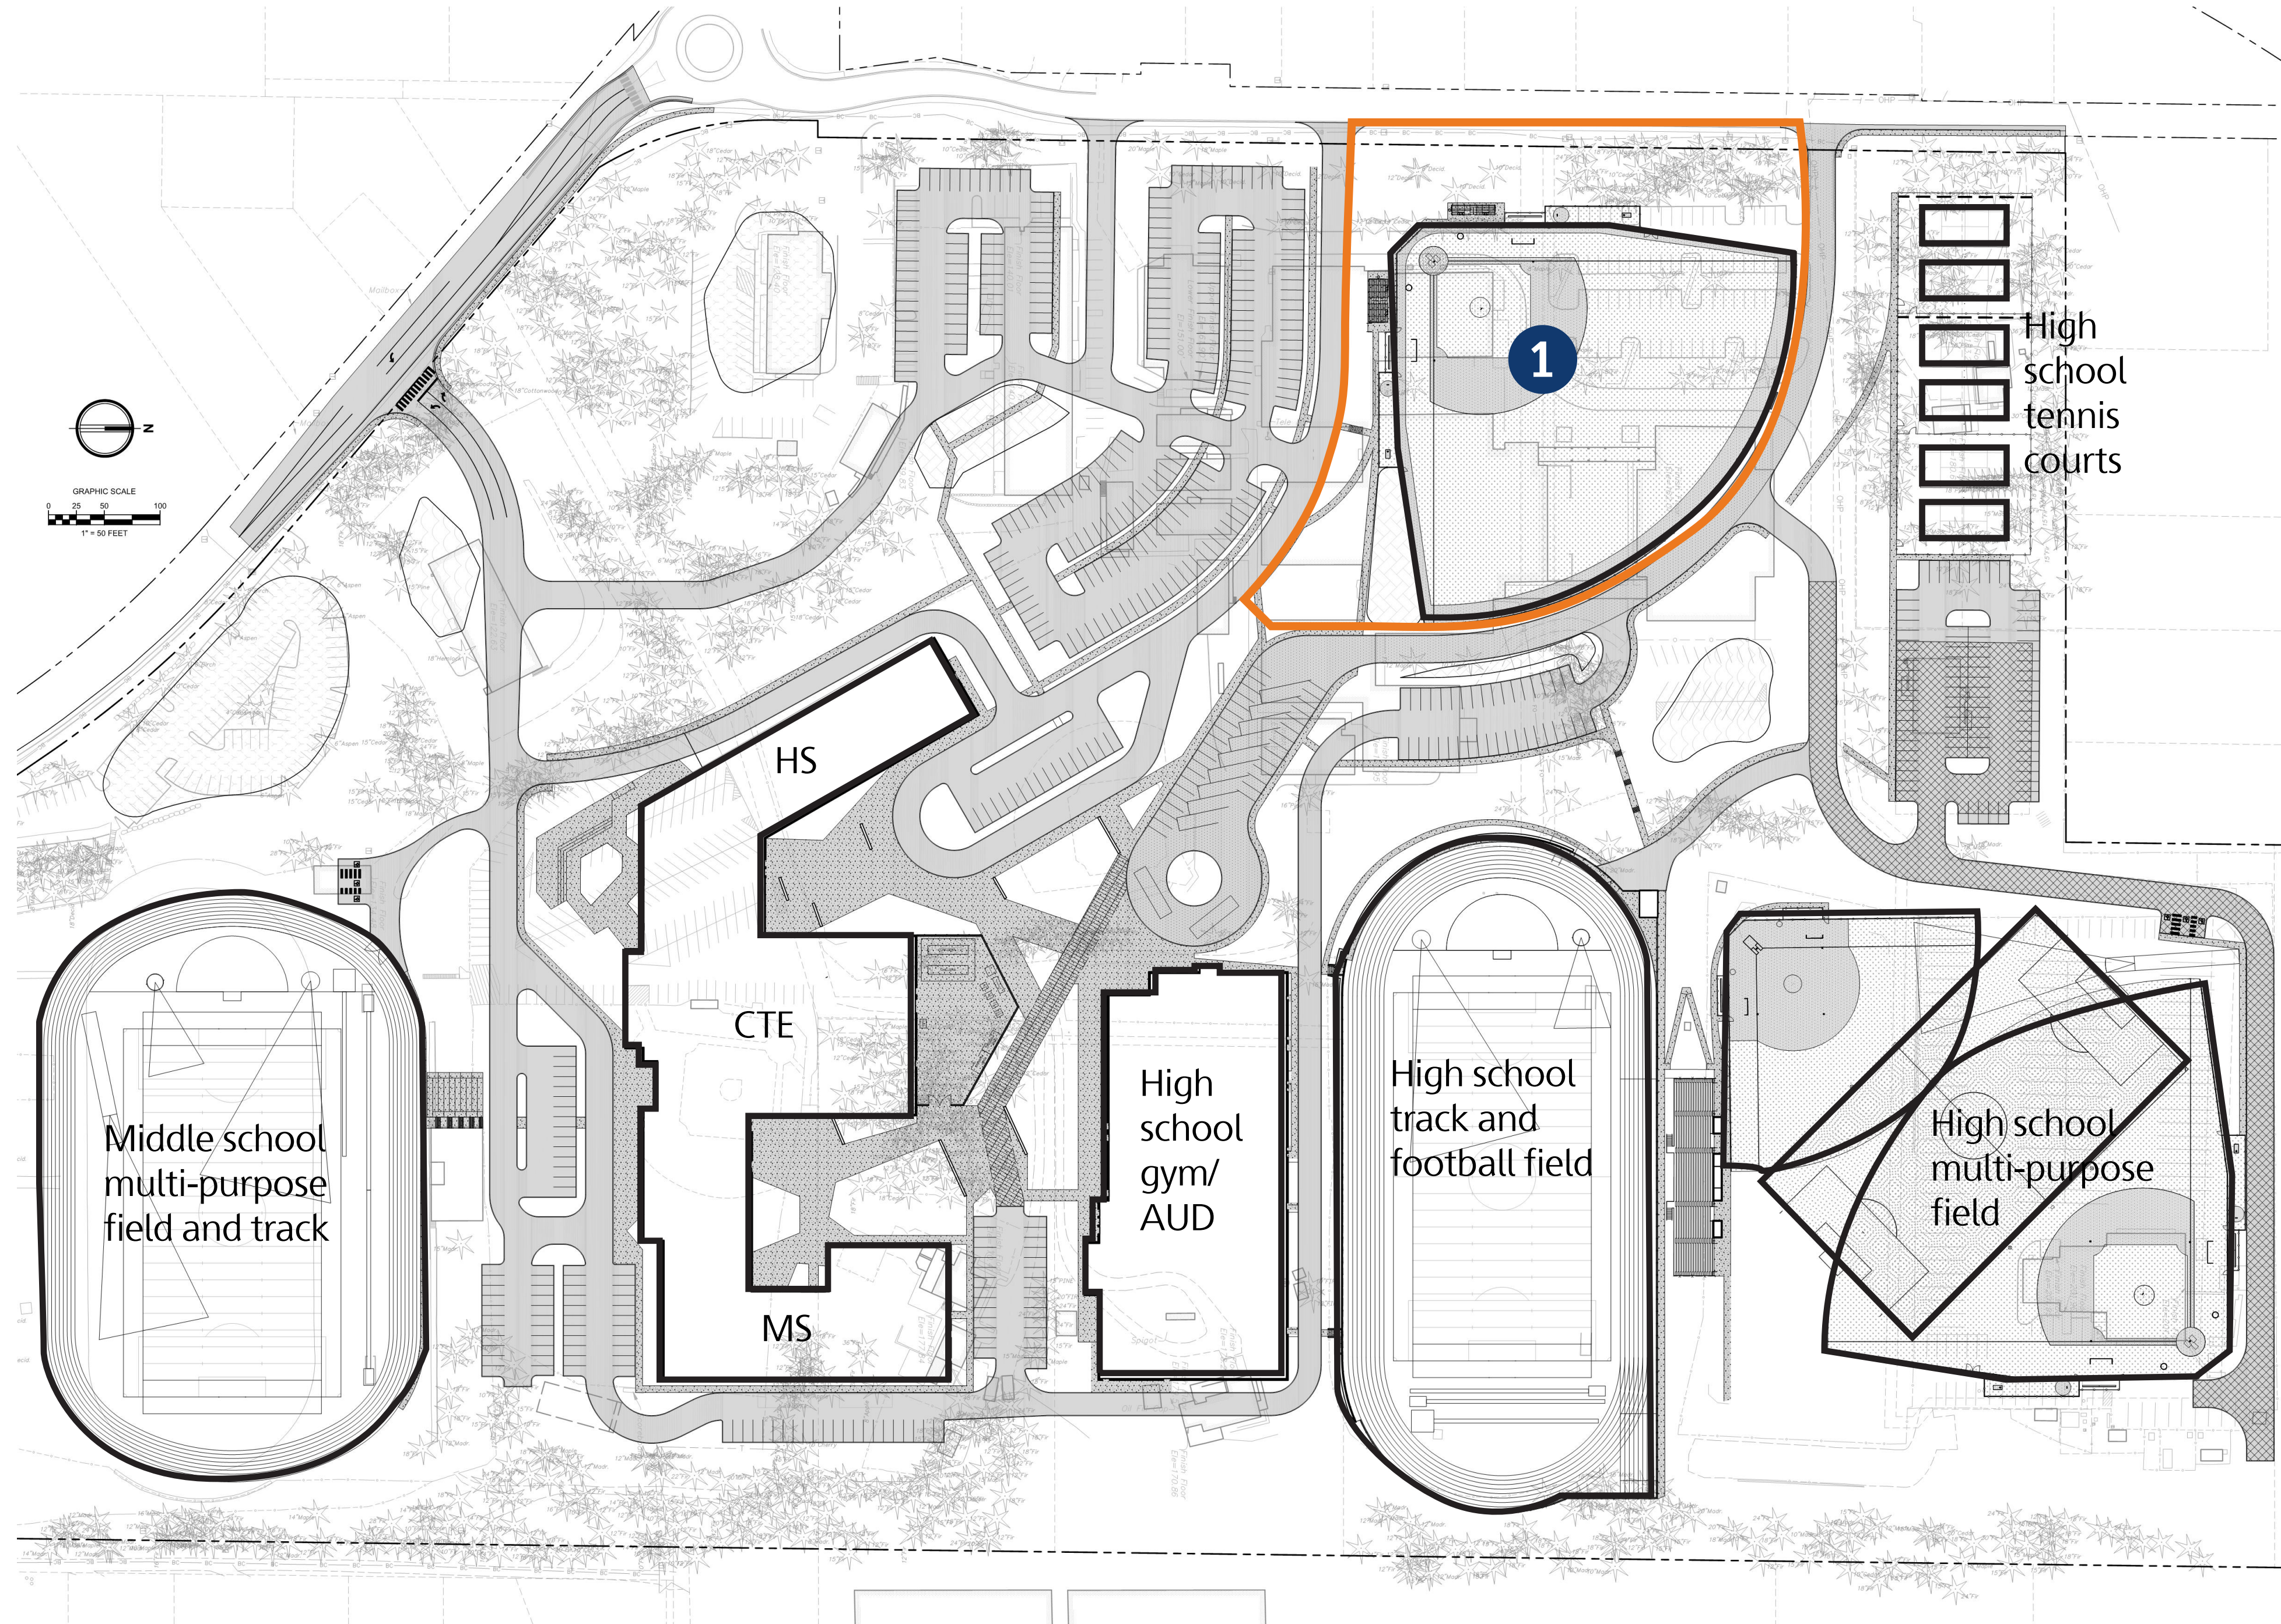

Phase 5:

- 1 Construct new baseball/softball fields.
